



Construction activities performed during the Week of 03/12/2017 – 03/18/2017 are listed below:

- Texas Sterling completed the concrete box culvert extension on the west (upstream) side of Culvert 5, north of Oyster Creek Dr.
- Frontier Communications (formerly Verizon) was onsite to continue installing span wire and poles along the west ROW between FM 2770 and Onion Creek.
- PEC began locating their existing utility line for proposed pole installation south of Oyster Creek Dr.
- Spectrum (formerly Time Warner Cable) were not onsite this week.

Anticipated activities for the next week are as follows:

- Texas Sterling to continue the concrete box culvert extensions for Culverts 3, 4, and 5.
- Frontier to continue installing span wire on the west ROW between FM 2770 to Onion Creek and schedule a splicing date to energize the new lines.
- PEC to complete relocating electric lines between Oyster Creek and Elm Grove Elementary and to continue removing electric lines no longer in use.
- Spectrum (Time Warner Cable) to schedule a splicing date to energize the new lines.

If you have any questions during the construction of this project please contact my assistant, Jennifer Scott, at 512-262-2091, or check the project website, www.improve1626.com . Thank you for your patience during the construction of these much needed improvements.

Thank you,

Mark Jones
Commissioner
Precinct 2





1. Sterling Placing Steel for Proposed Box Culv N of Oyster Creek




2. Sterling Placing Steel for Proposed Box Culv N of Oyster Creek



3. Sterling Pouring Wall of Proposed Box Culv N of Oyster Creek



4. Frontier Installing Span Wire N of Mustang Creek

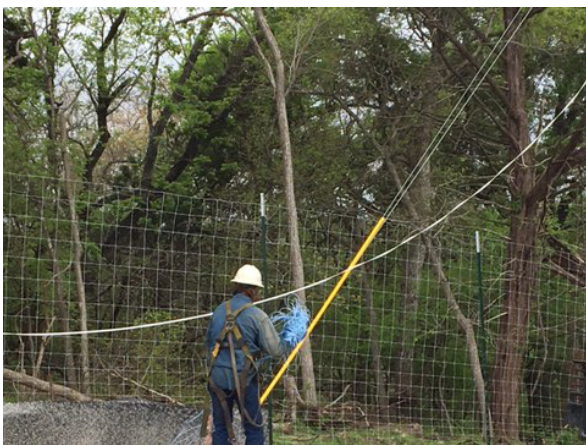

5. Frontier Installing Span Wire S of Mustang Creek
